



# SAN BRUNO RECREATION & AQUATIC CENTER

Advisory Committee Update

June 15, 2022



# AGENDA

## 1. Construction Update and Look Ahead Schedule

- a) Project Information Update
- b) Completed To Date
- c) Change Order Report / Budget Update
- d) Schedule Update
- e) What's Happening Next 30 Days

## 2. Questions

# Construction Update and Look Ahead Schedule



## PROJECT INFORMATION



**Start Date:** September 2021




**Project Completion:** Fall 2023



**Estimated Cost Completed To Date:** 18.39% (May 2022)



**EarthCam Link:** [https://share.earthcam.net/RecCenterBuild/rec\\_center\\_build/camera/view\\_1](https://share.earthcam.net/RecCenterBuild/rec_center_build/camera/view_1)

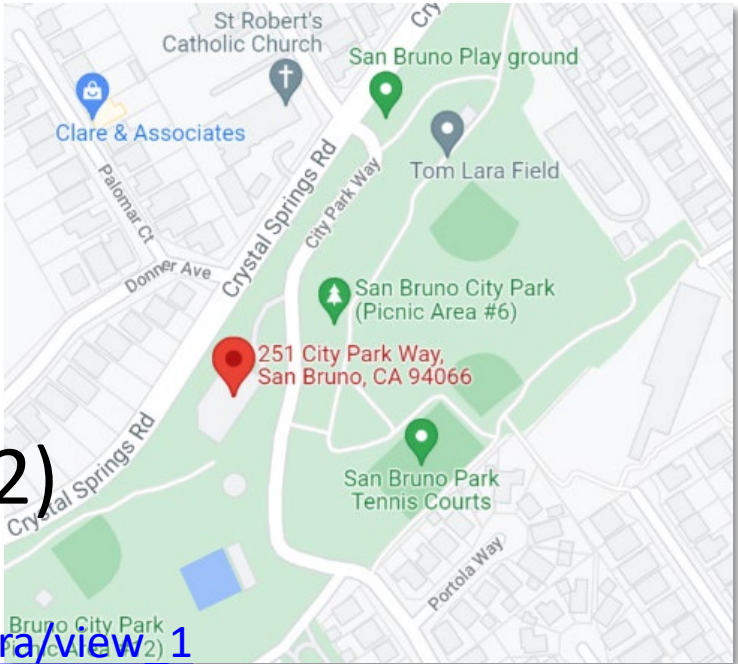

# Construction Update and Look Ahead Schedule

## COMPLETED TO DATE (Through 06/15/22)



May 17, 2022



June 15, 2022



# Construction Update and Look Ahead Schedule

## *COMPLETED TO DATE (Through 06/15/22)*



**BUILDING  
FOUNDATIONS  
EXCAVATIONS AND  
REINFORCING  
BARS**



# Construction Update and Look Ahead Schedule

## *COMPLETED TO DATE (Through 06/15/22)*



**BUILDING FOUNDATION EXCAVATIONS  
AND REINFORCING BARS**



# Construction Update and Look Ahead Schedule


## *COMPLETED TO DATE (Through 06/15/22)*



**BUILDING FOUNDATION EXCAVATIONS  
AND REINFORCING BARS**



## Change Order Report

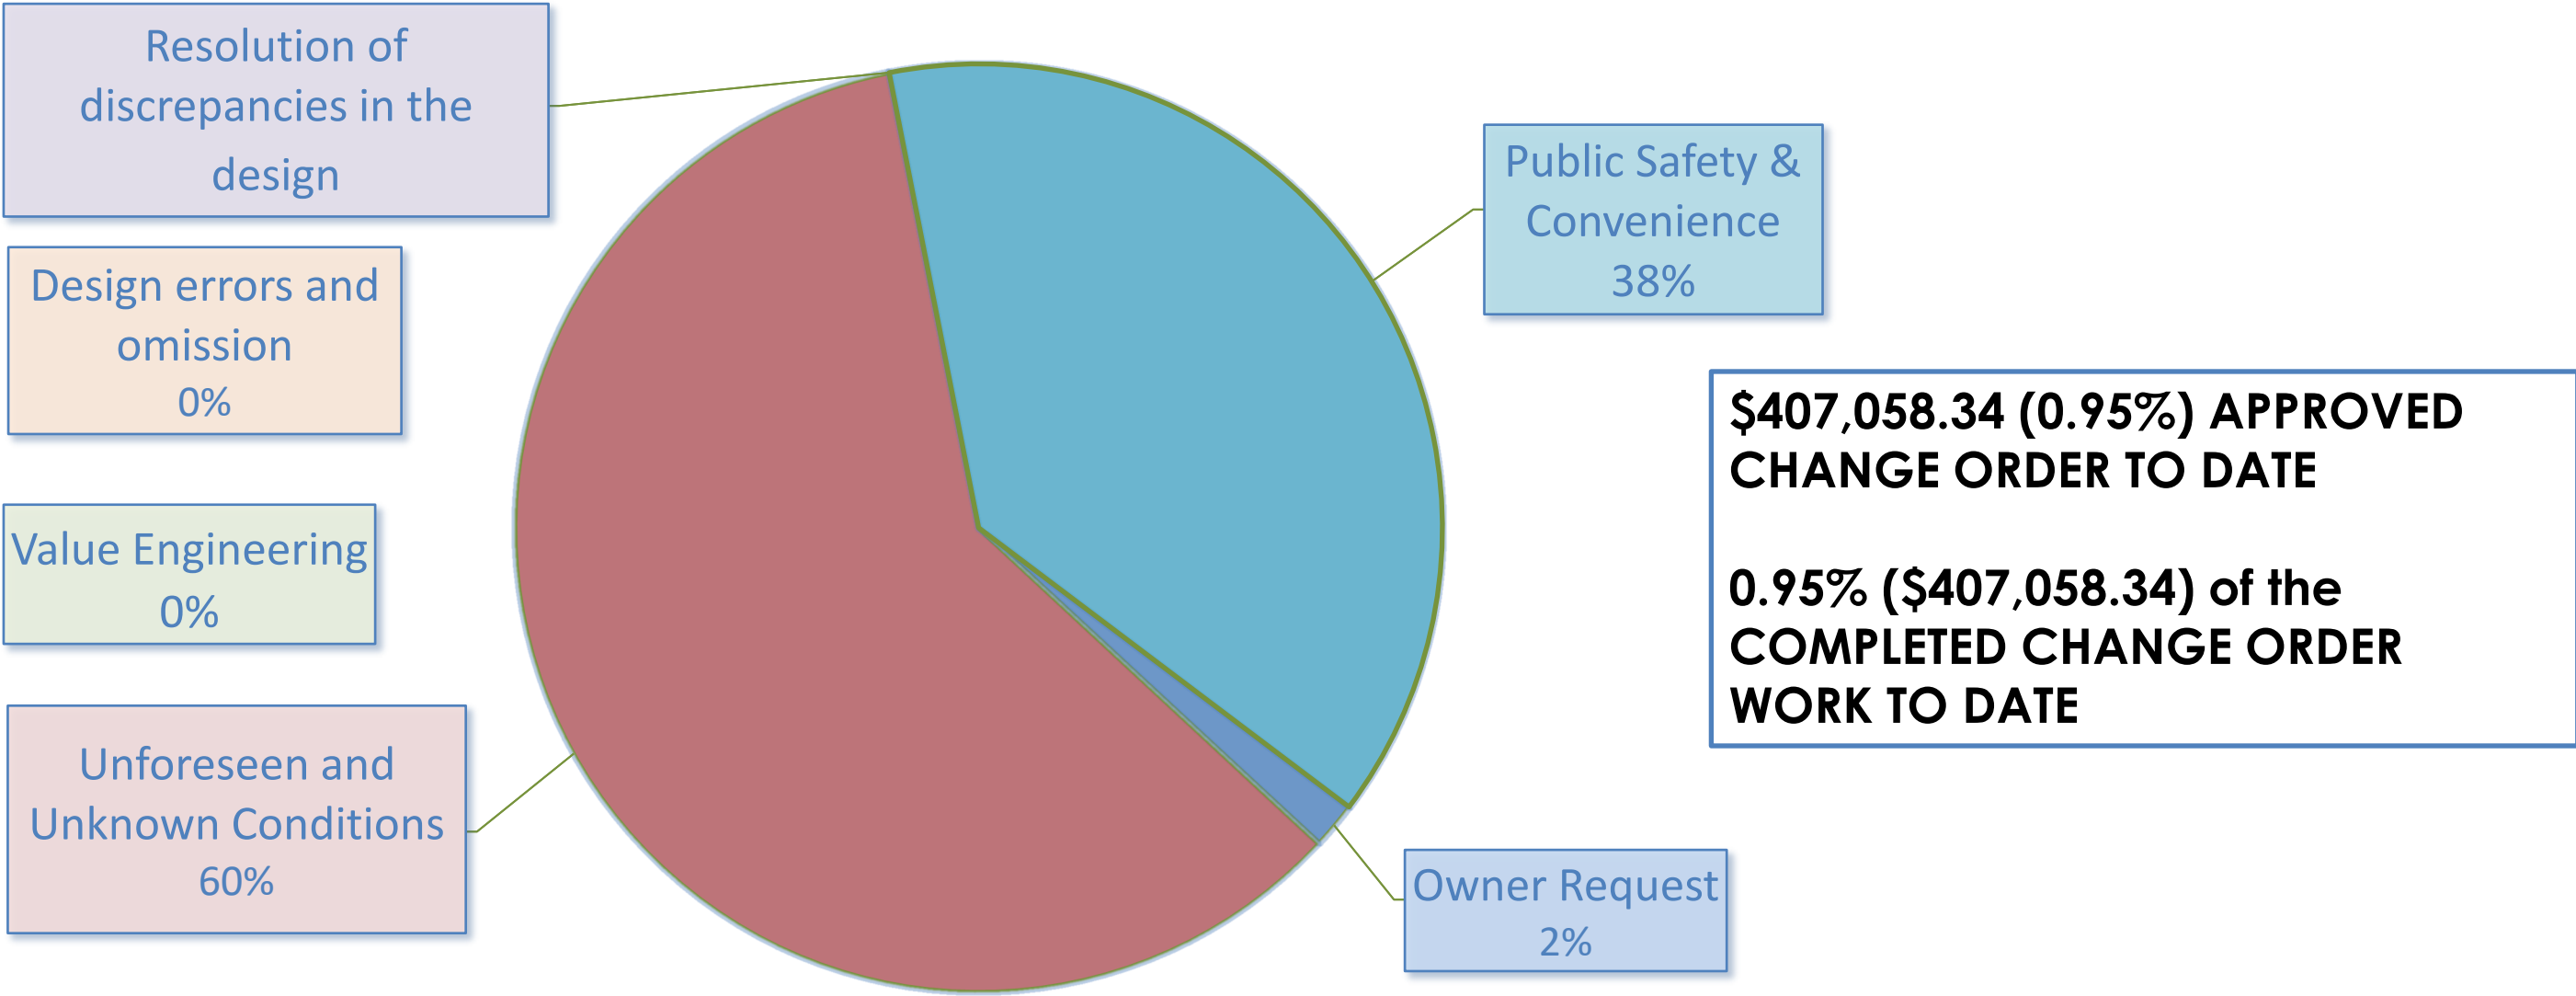

# Construction Update and Look Ahead Schedule



## Project Budget Update

### Total Project Budget:

- \$60,540,228.00

### Total Expenses To Date:

- \$16,141,124.15 (26.66%)

### Pre-Construction Cost Total:


- \$6,814,010.20

### Construction Cost To Date:


- \$9,327,113.95

### SOFT COSTS

- Design (Group 4)
- Environmental
- Project Manager (CPM Associates)
- Construction Manager (Griffin Structures)
- Geotechnical, T&I, Waterproofing, Commissioning Services
- Lara Field Parking Lot
- Traffic Signals, Sewer, Water, Sidewalk, CityNet Fiber
- Temporary Space During Construction
- Furniture Fixtures and Equipment
- Electronic systems and special equipment
- Utility company connection and services
- Fees/ Administration/ Business Plan

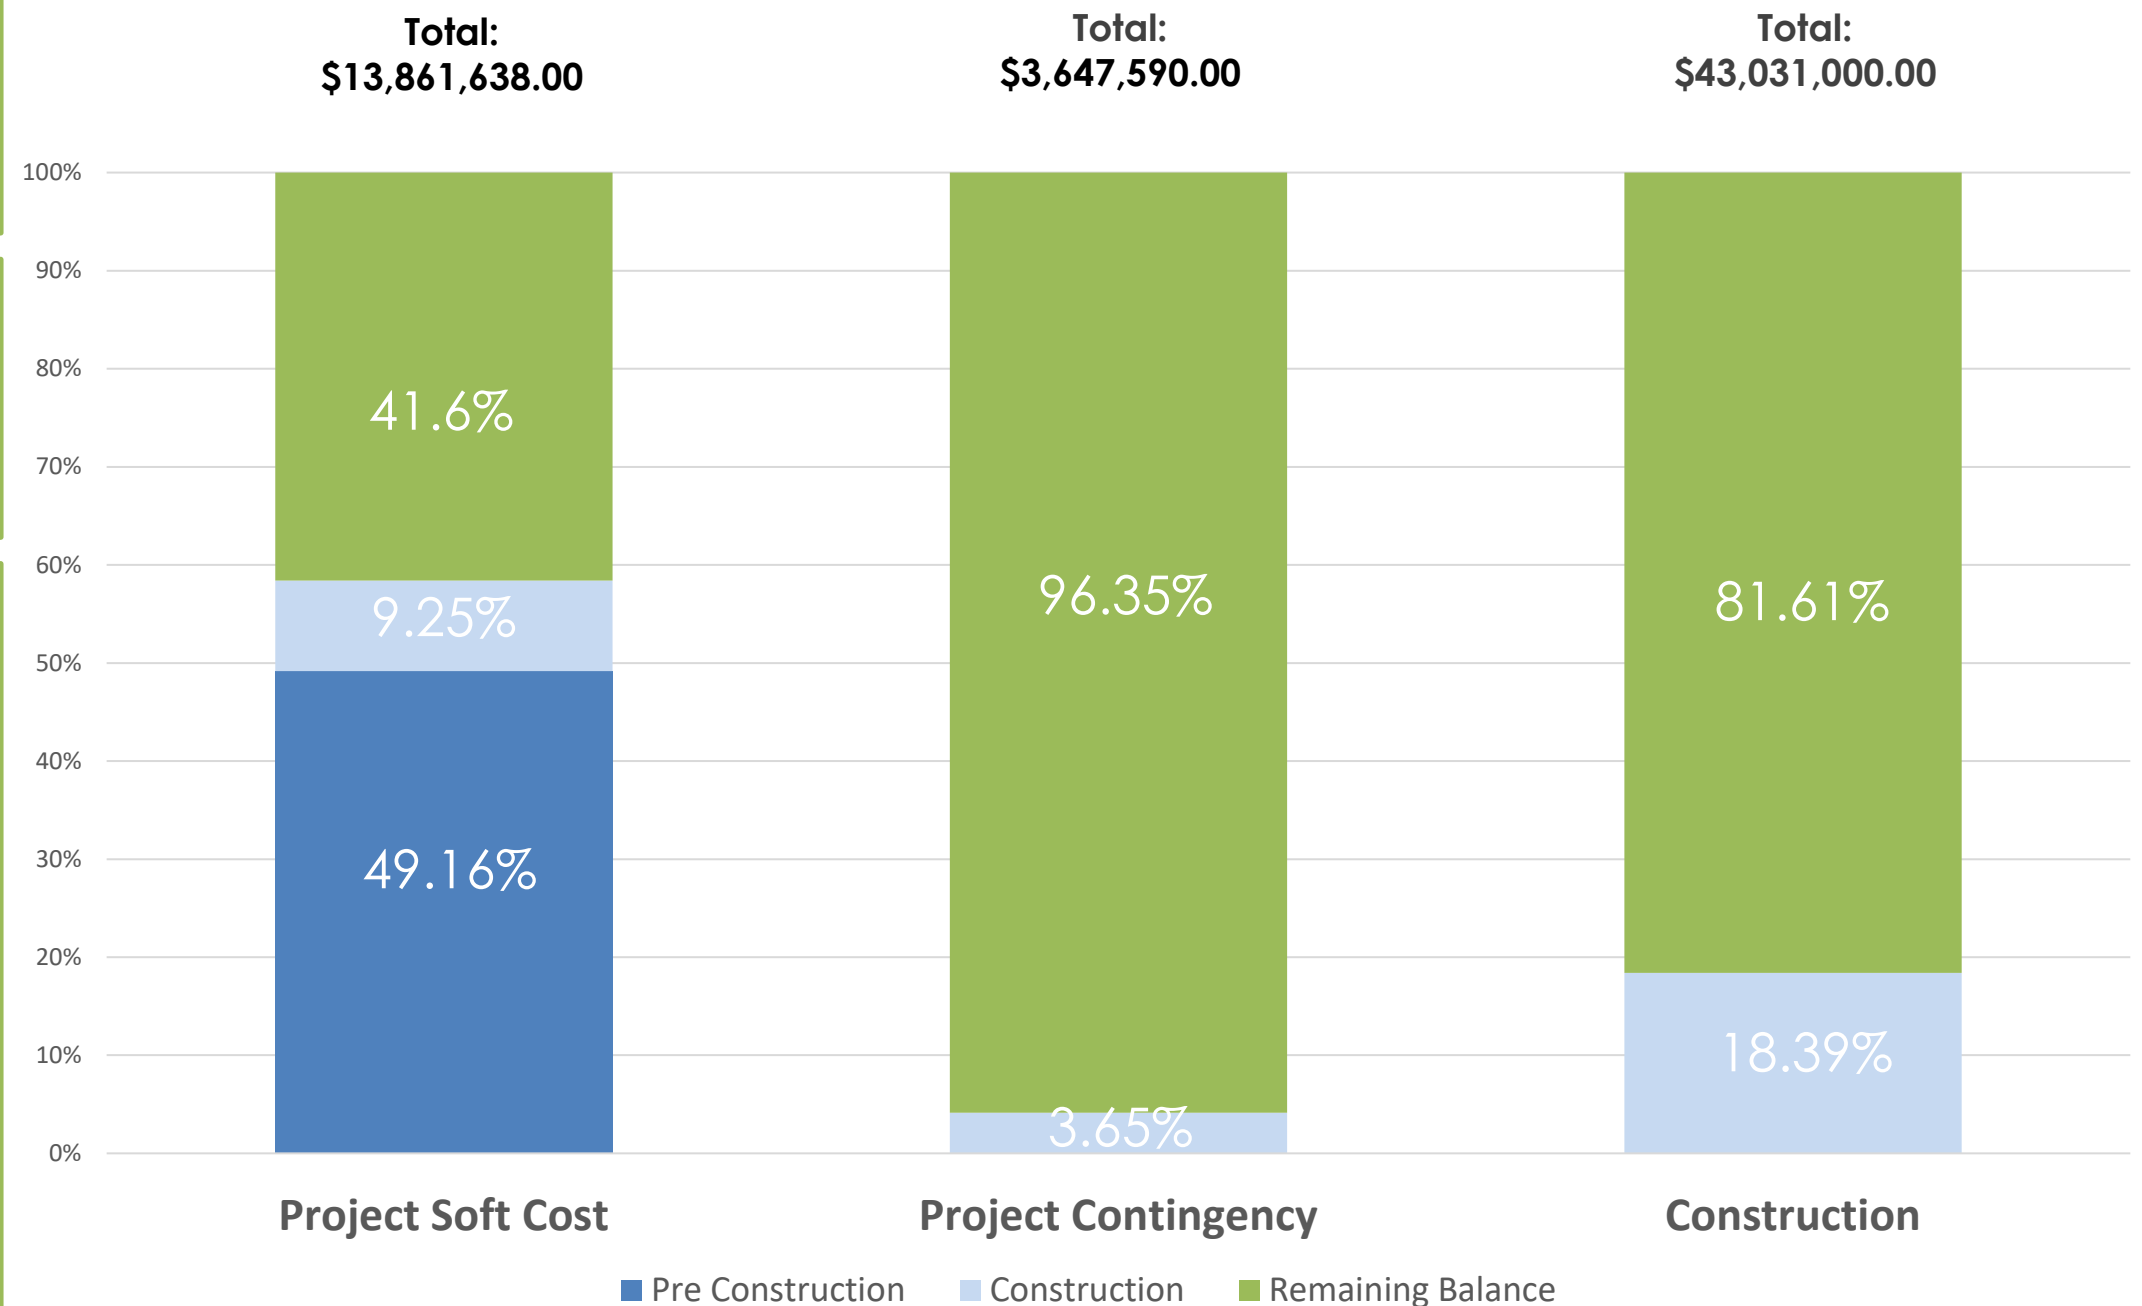


# Construction Update and Look Ahead Schedule

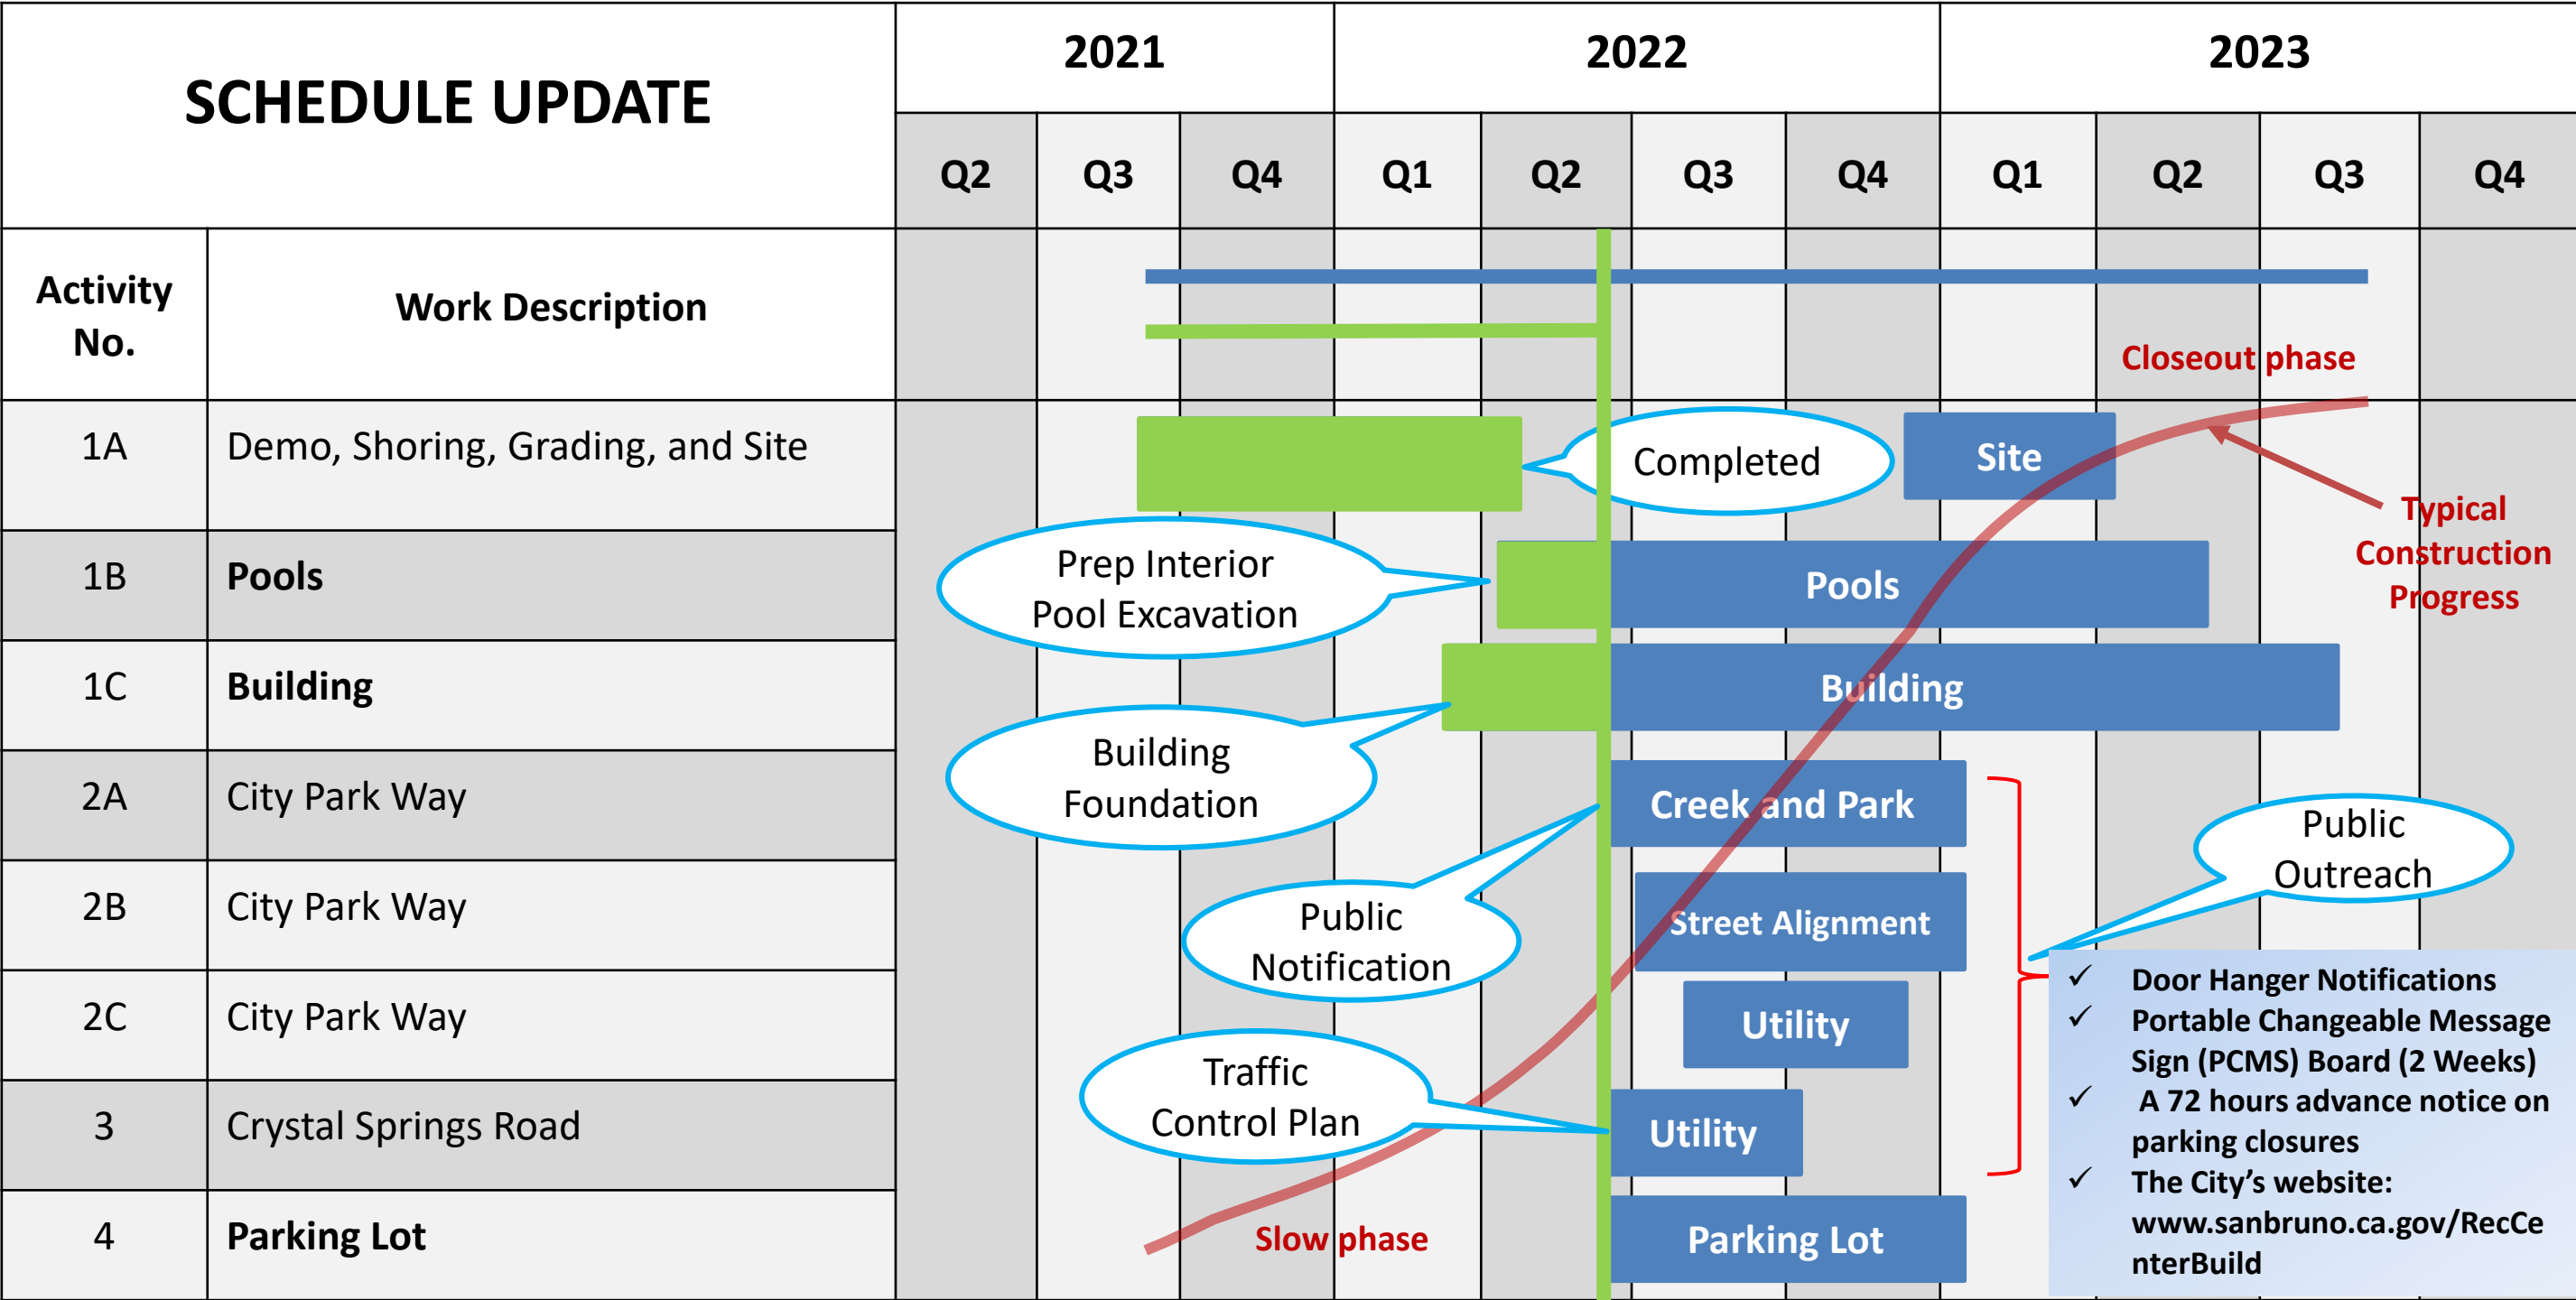

# Construction Update and Look Ahead Schedule

## *WHAT'S HAPPENING NEXT 30 DAYS?*

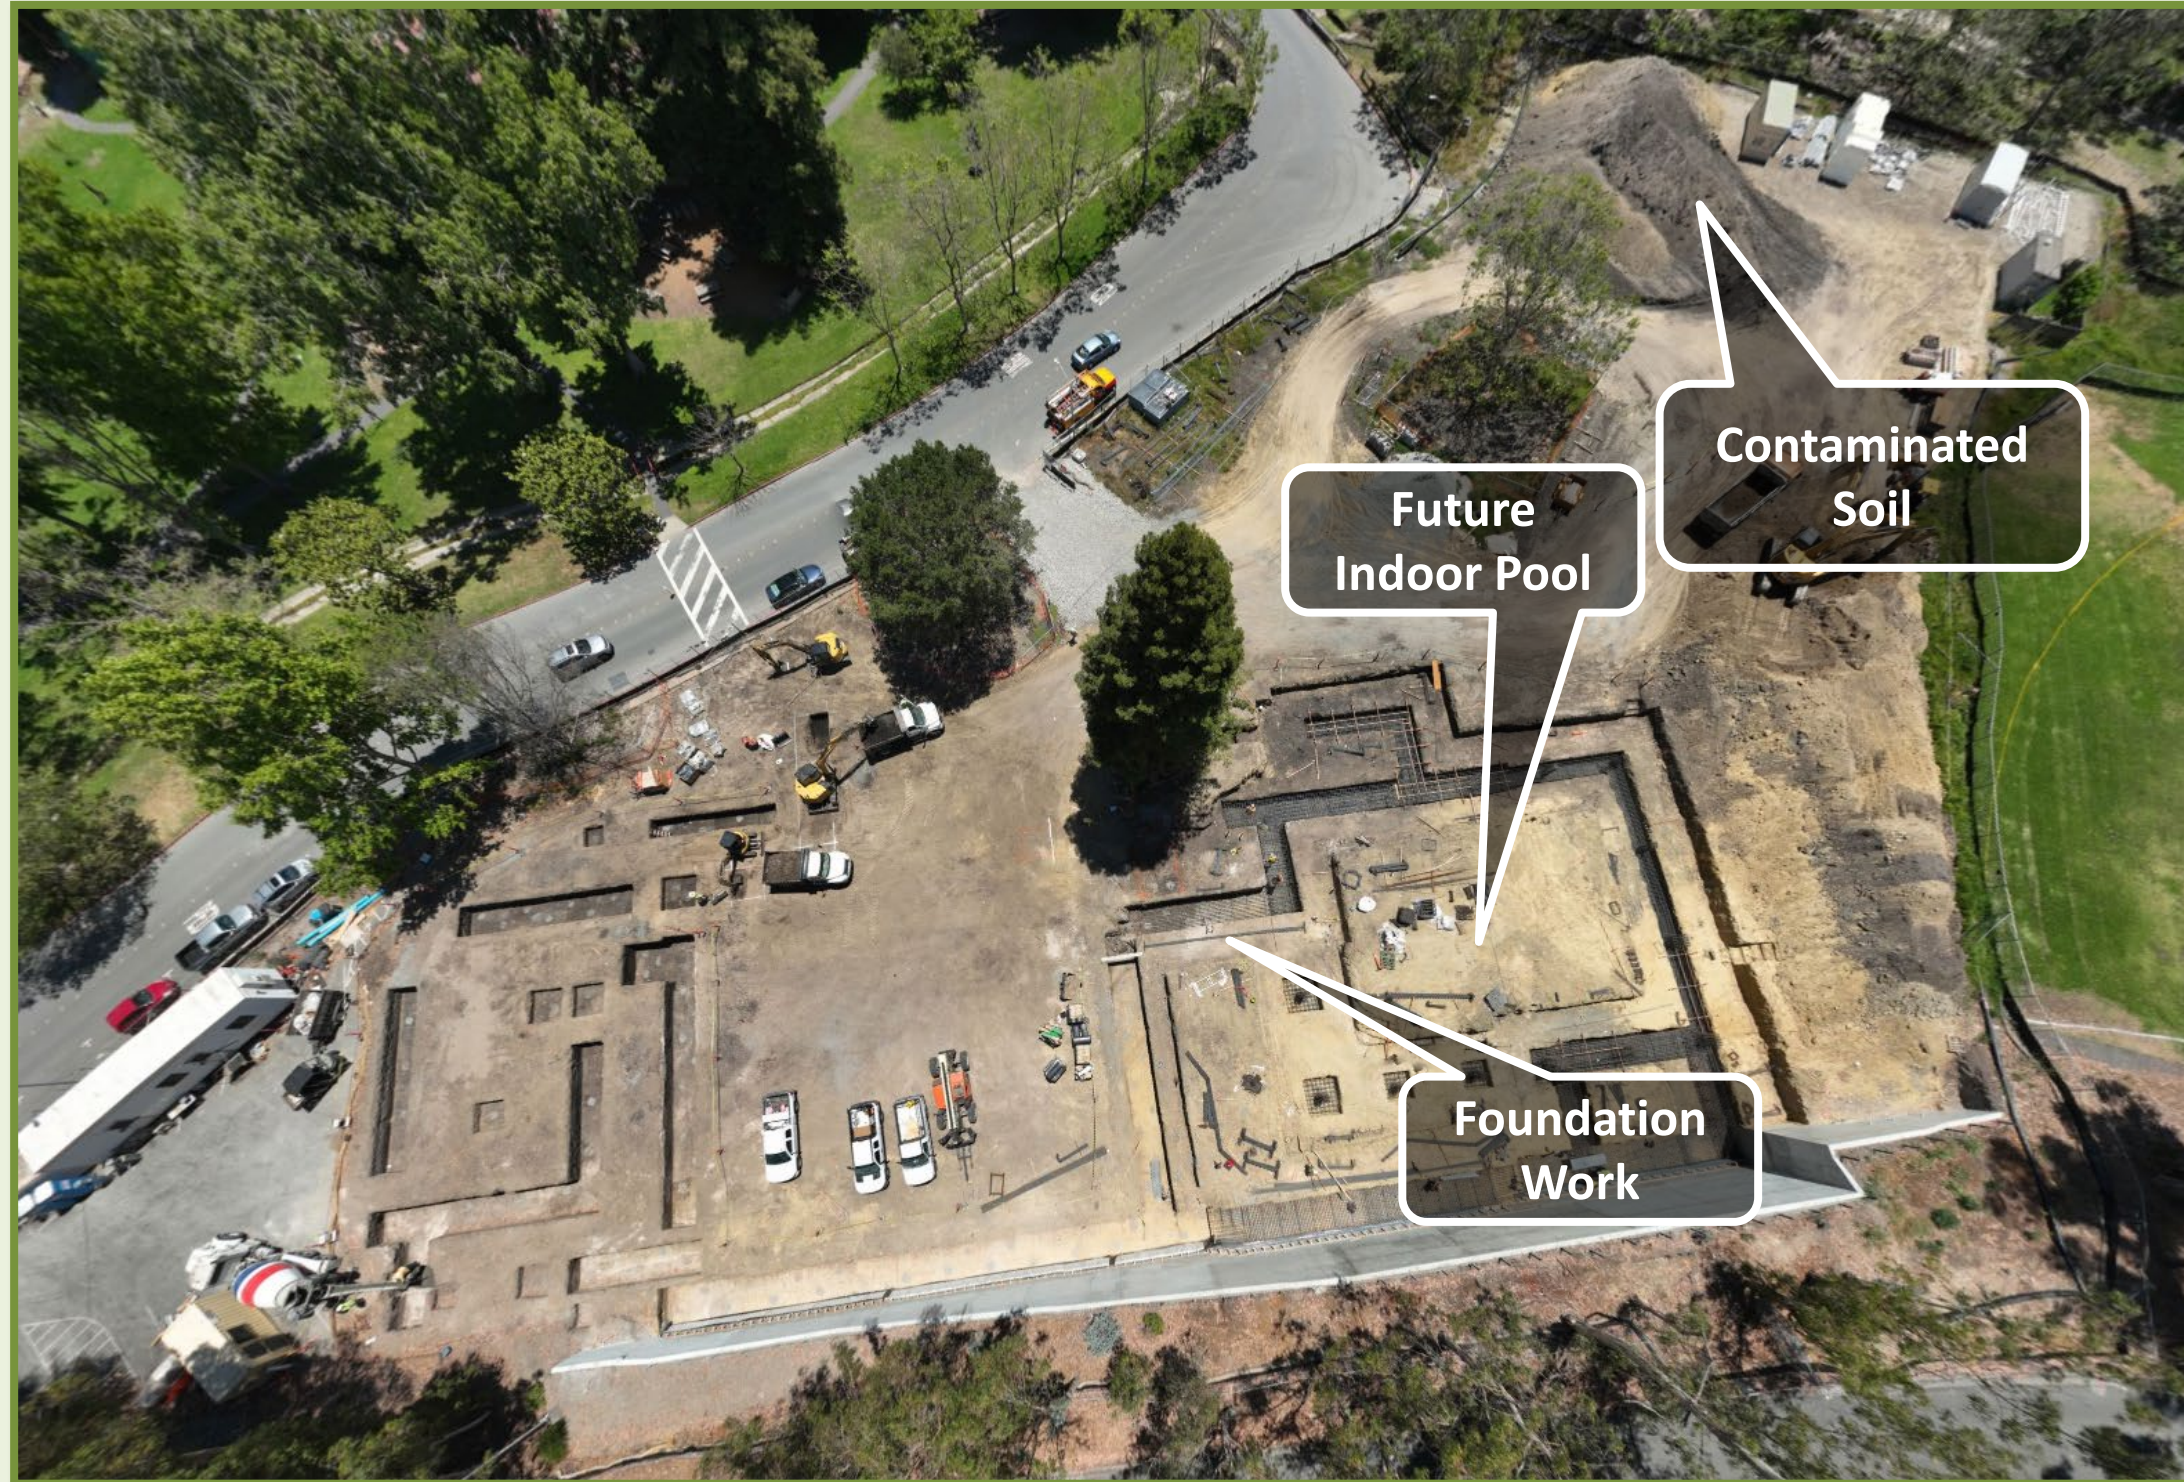


### ONSITE WORK

- Foundation Work
- Pool Related Work
- Under Slab Utility

# Construction Update and Look Ahead Schedule



## WHAT'S HAPPENING NEXT 30 DAYS?

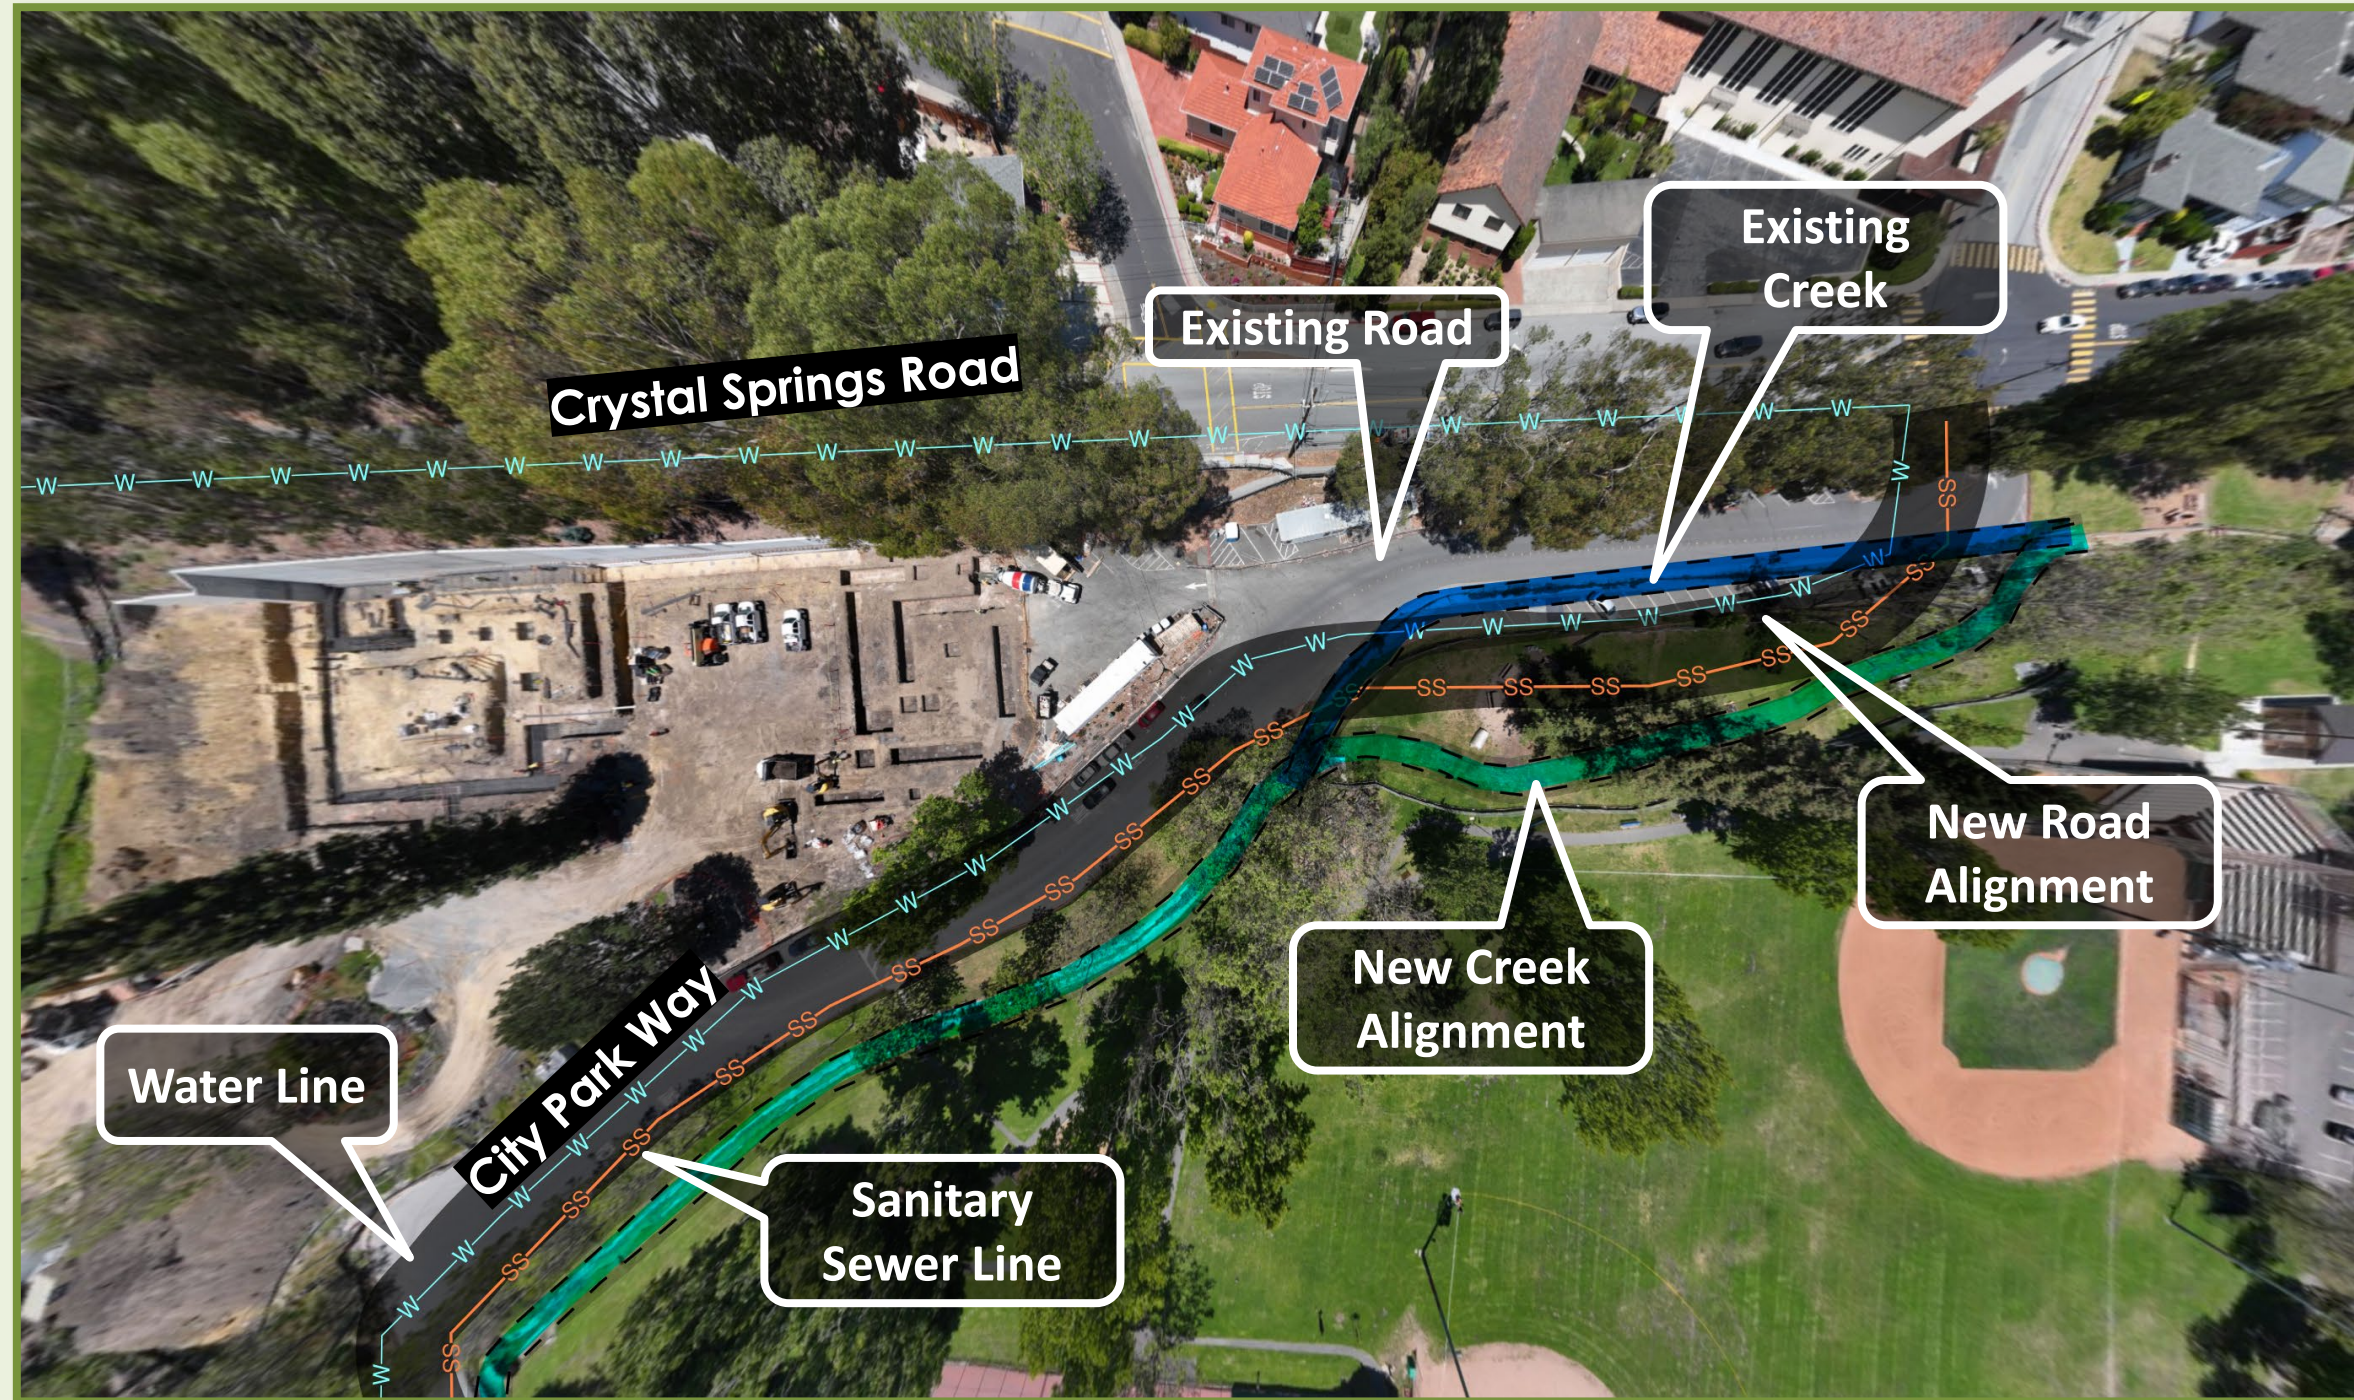


### OFFSITE WORK

- Start Creek Realignment
- City Park Way Realignment
- Street Utility Work (Water, Sewer & Storm)
  - Start Crystal Spring Water Line
- Public Outreach
  - Partial Park Closure
  - City Park Way Closure
  - Crystal Spring Lane Closure



# Construction Update and Look Ahead Schedule

## *WHAT'S HAPPENING NEXT 30 DAYS?*

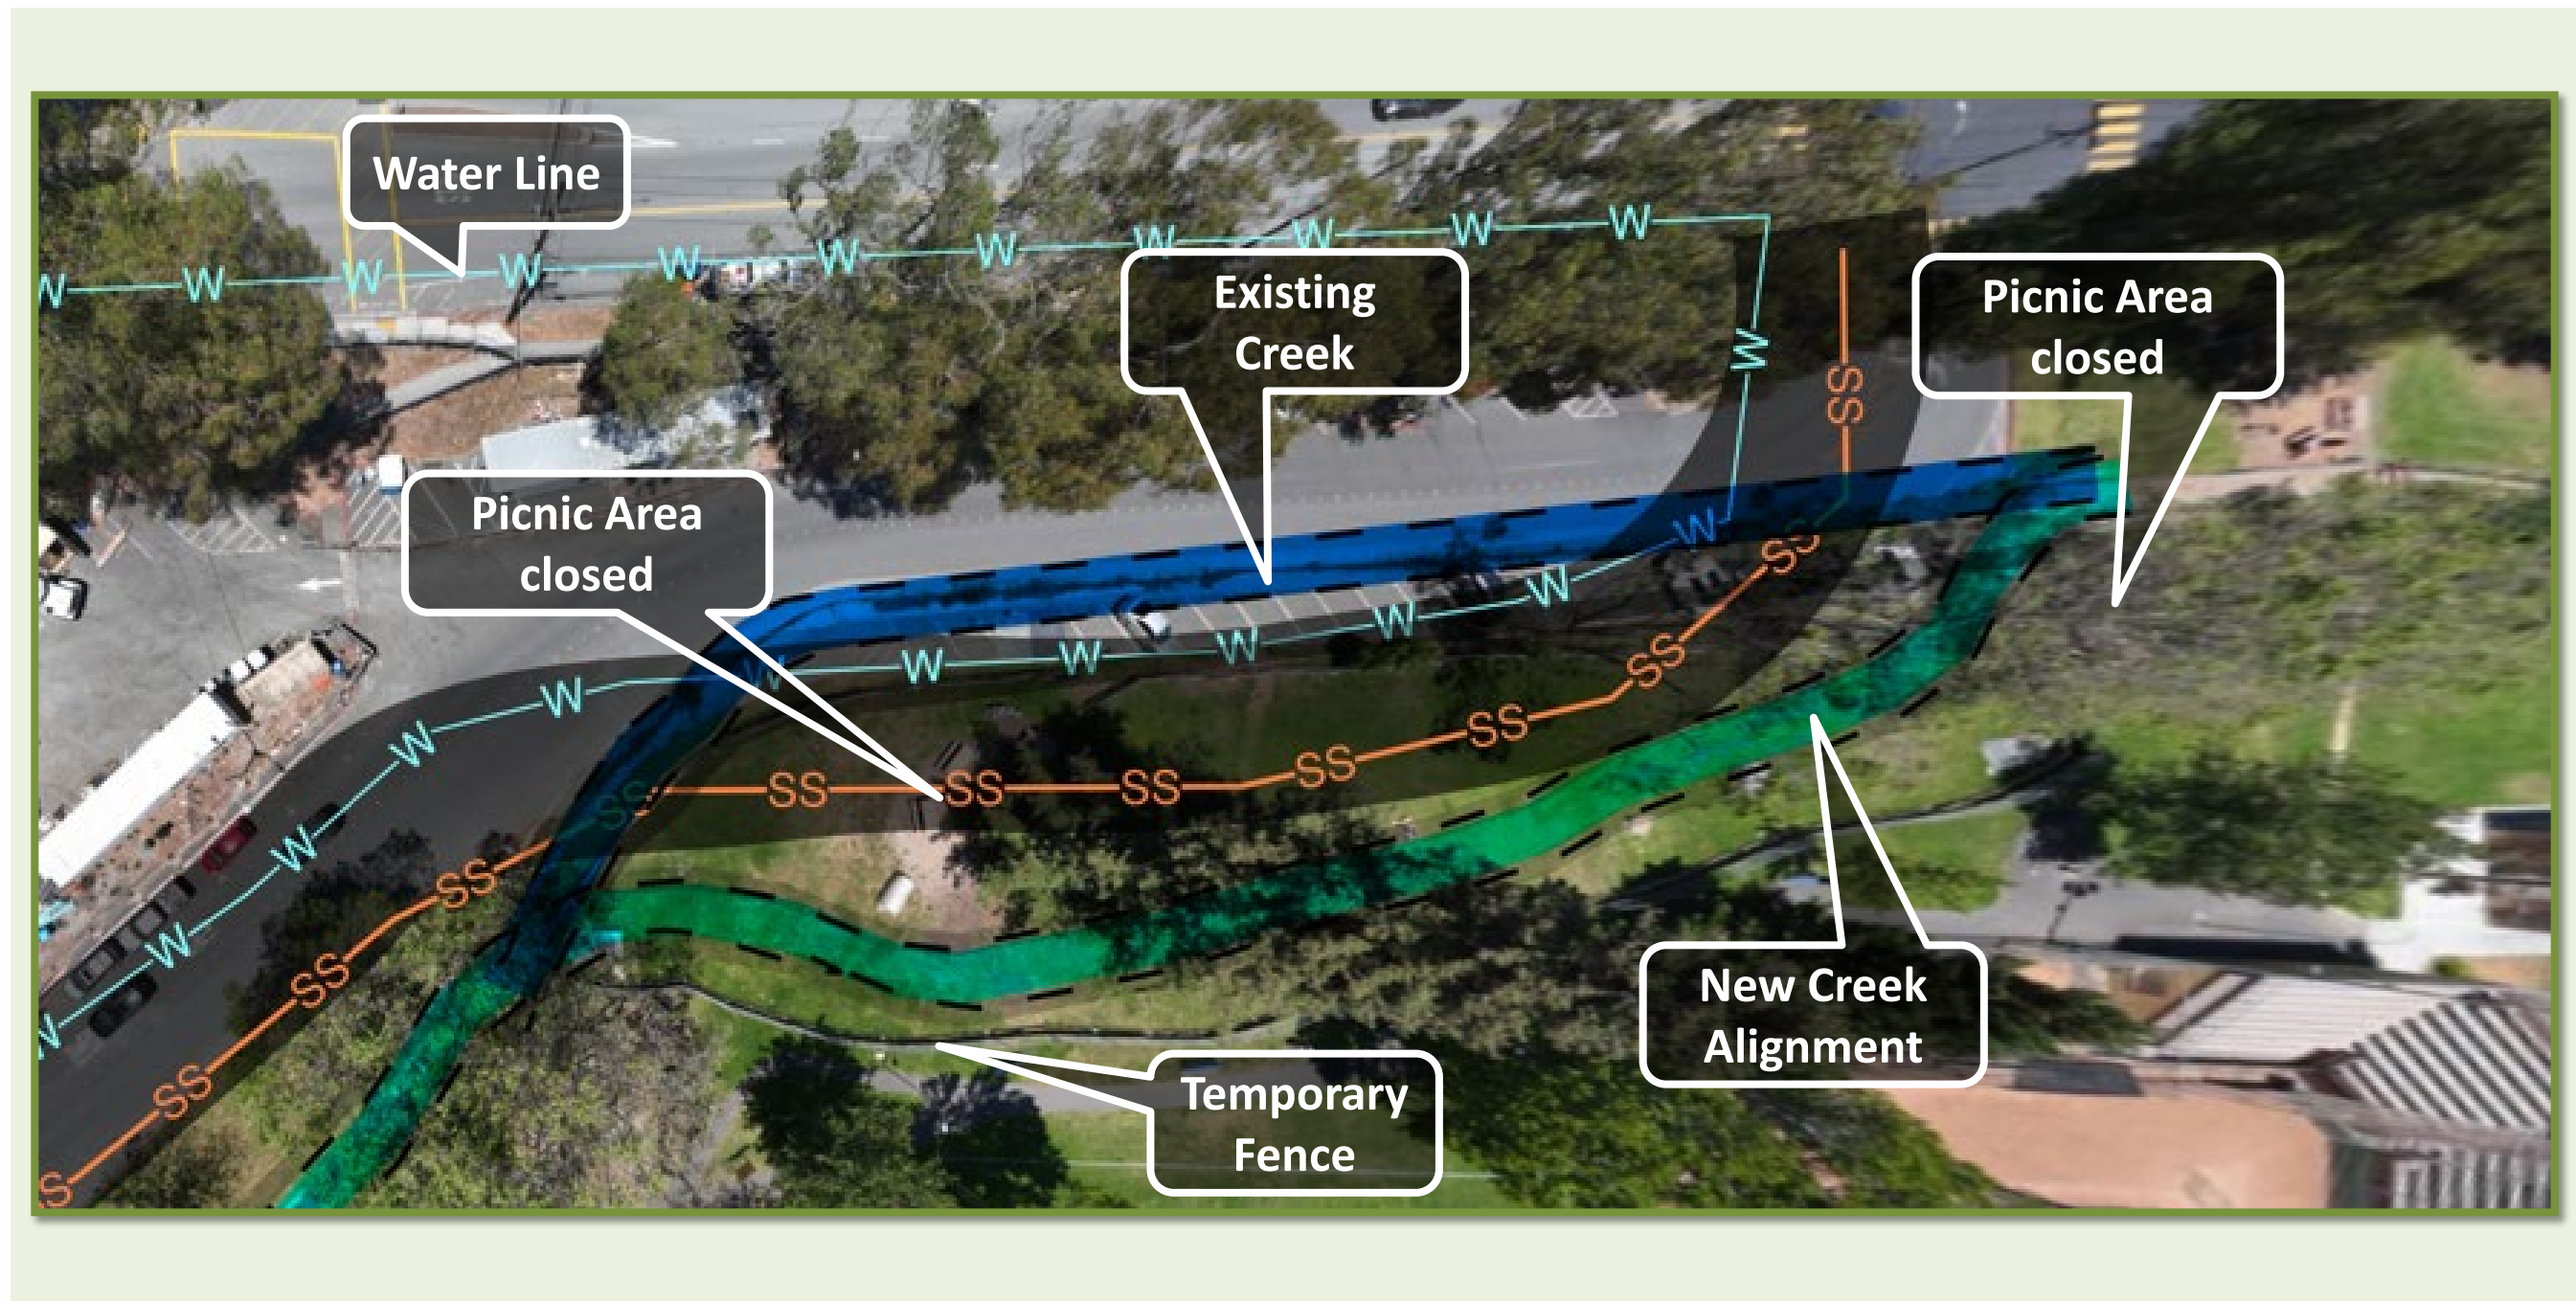

# THANK YOU

[sanbruno.ca.gov/RecCenterBuild](https://sanbruno.ca.gov/RecCenterBuild)
